

JEFFERSON TOWNSHIP DEPARTMENT OF HEALTH Application for Permits

(FOR OFFICE USE ONLY)

OWNER <u>[REDACTED]</u>	BLOCK <u>162</u>	SEWAGE <u>75-144A</u> ^{20.00}
<u>96 EAST SHORE RD., Lk Hopatcong</u> (Address)	LOT <u>27</u>	WATER
(Telephone) <u>[REDACTED]</u>	ZONE	PLUMBING
CONTRACTOR <u>WOOD BUTCHERS</u>	SECTION	BOILER
<u>16 SHAWNEE PKWY, WHARTON, N.J. 07885</u> (Address)	STREET <u>EAST SHORE RD.</u>	HOT WATER
(Telephone) <u>07885</u>	NO. OF BEDROOMS <u>2</u>	OTHER

ENGINEERING DEPARTMENT

1. ALL DRAINAGE REQUIREMENTS HAVE BEEN MET AND INCORPORATED INTO THIS PLOT PLAN AND, AS SHOWS, WILL NOT CREATE A DRAINAGE PROBLEM.

2. STREET: 1. Improved ☒ Unimproved ☐
 2. Township Road ☒ Public R.O.W. ☐ Private Lane ☐
 3. Road Bond Required YES ☐ NO ☒
3. THIS PLOT PLAN IS PART OF A SUBDIVISION AND IS IN COMPLIANCE WITH ALL PLANNING BOARD REQUIREMENTS.
 YES ☐ DOES NOT APPLY ☒

Request by Designer

HEALTH DEPARTMENT VARIANCE NEEDED

YES ☒ NO ☐

BOARD OF ADJUSTMENT VARIANCE GRANTED

YES ☐ NO ☐

BUILDING & ZONING DEPARTMENT

I hereby certify that the attached Plot Plan meets all requirements of the Zoning Ordinance. I have reviewed the Building plans and find them to be satisfactory. The number of bedrooms is correct. Without major alterations other rooms could not be used as additional bedrooms.

Building and Zoning Officer

HEALTH DEPARTMENT

NOTE: ALL DETAILS OF CONSTRUCTION MUST BE SHOWN ON A SEPARATE SHEET.

PHONE 875-7600

SEWAGE: New ☐ Repair ☒ CONTRACTOR JOHN CLARK, BERKSHIRE VALLEY RD, WHARTON, N.J.

1. Depth of soil log	<u>10'</u>	5. No. of holes	<u>1</u>
2. Depth of ledge	<u>NOT ENCOUNTERED</u>	6. No. of saturations	<u>3</u>
3. Depth of water	<u>NOT ENCOUNTERED</u>	7. Stabilized rate	<u>4 min./inch.</u>
4. Depth of perc test	<u>4'</u>	8. Distance between pits	<u>N/A</u>

Type of soil encountered 0'-6" TOPSOIL, 6"-2' FINE LOAM FILL; 2'-2.5' TOPSOIL & HUMUS; 2.5'-10' FINE SANDY LOAM, SOME SILT & ROCKS

Liquid Disposal Bed Size 7' DIAM. X 6' DEPTH Pit ☒ No. 1

Septic tank capacities () (750 GAL. NO. 1)

WELL: NEW ☐ DEEPENING ☐ WATER CONNECTION: ☐ CONTRACTOR Paul E. Arabia N.J. RE. 21249

Design Engineers signature and License No..

- | | |
|--------------------------|--------------------------------------|
| 1. No. of feet of casing | 5. Distance from nearest septic tank |
| 2. Casing wall thickness | 6. Dwellings served |
| 3. Casing diameter | 7. Driller's license & type |
| 4. Method of sealing | |

PLUMBING & HEATING: NEW ☐ ALTERATION ☐ CONTRACTOR

Bathtubs	Kitchen Sinks	Dishwashers	Garbage Disposals
Wash Basins	Showers	Toilets	Urinals
Slop Sinks	Washing Machines	Water Fountains	Bidets
Laundry Trays	All others	TOTAL FIXTURES	
BOILERS	FURNACES	WATER SOFTENERS	HOT WATER HEATERS

We hereby grant permission to the above applicant to locate and/or construct or alter as per application and attached drawings. Plumbing, sewage, water and other things as shown. We do certify that this application is in compliance with all ordinances with which we are charged, EXCEPT where variances have been indicated.

PLUMBING DEPT.

DIRECTOR

Carl Weber 9/16/75
9-16-75

BLOCK

162

LOT 2

LOT 6

LOT 1

N 64° 49' W 50'

LOT 27

LOT 26

NOTE:

1) EXTEND SEPTIC TANK ACCESS
OPENING TO WITHIN 12"
OF FINISHED GRADE.

O WELL

EXISTING
DWELLING

2) DISTANCE
FROM WELL TO
SEPTIC TANK
IS 48' ±.

GARAGE

CONCRETE
BLOCK WALLROCK
OUT-
CROPEXISTING
WELL

EXISTING
2 BR
DWELLING
4" INV.
EL. 90.2

INSTALL
NEW
CLEANOUT

EXISTING
DWELLING

SEPTIC TANK 4" CIP.
INV. ELV. 86.0

750 GAL SEPTIC TANK
SEEPAGE PIT 7' DIAM.
6' DEPTH BELOW INLET
SEEP PIT INV. EL. 85.5

S 25°-01' W

STONE
DRIVEWAYCONC.
SLAB

PIT

4" CIP
PIPE

EXISTING
SEPTIC
SYSTEM

EXISTING
SEPTIC SYSTEM
TO BE REMOVED
OR BACKFILLED AS
REQUIRED.

S 64°-59' E 50'

EAST SHORE ROAD


23' ± EXISTING PAVEMENT

ALTERATION OF EXISTING
SEPTIC SYSTEM FOR 2 BED-
ROOM DWELLING AT
96 EAST SHORE ROAD
JEFFERSON TWP., N.J.
PREPARED BY: Paul T. Sabia

PAUL T. SABIA
N.J.P.E. 21249

● LOCATION OF TEST HOLE & PERC TEST.

SCALE: 1" = 20'
DATE: 9/14/75



NOTE: SEPTIC SYSTEM TO BE
CONSTRUCTED IN STRICT
ACCORDANCE WITH JEFFERSON
TWP. BD. OF HEALTH REQUIREMENTS
& N.J. P.L. 1954, CHAPTER 199.


Paul T. Sabia
PAUL T. SABIA
N.J. RE. No. 21249

J.T. EXCAVATING, INC.

663-1479

LOT 27

BLK. 162

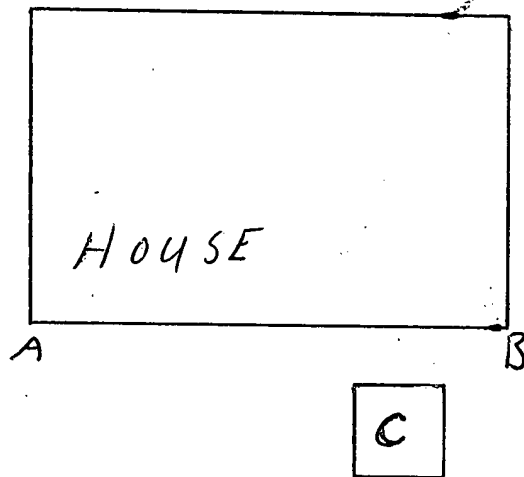

- 1000 gallon
concrete septic Tank C - A 32' B 11'
6'x6' seepage pit D - A 32' B 25'

o public
water

JEFFERSON TOWNSHIP

DEPARTMENT OF HEALTH

Application for Permits

Doord 10/14/86
(FOR OFFICE USE ONLY)

HEALTH DEPARTMENT VARIANCE NEEDED YES ☐ NO ☐
ENGINEERING DEPARTMENT I hereby certify that this Plot Plan is in compliance with any Planning Board or Board of Adjustment additional requirements and that all drainage requirements have been met and incorporated into this Plot Plan and, as shows, will not create a drainage problem. _____ Township Engineer
BOARD OF ADJUSTMENT VARIANCE GRANTED YES ☐ NO ☐
BUILDING & ZONING DEPARTMENT I hereby certify that the attached Plot Plan meets all requirements of the Zoning Ordinance. I have reviewed the Building plans and find them to be satisfactory. The number of bedrooms is correct. Without major alterations other rooms could not be used as additional bedrooms. _____ Building and Zoning Officer

BLOCK <u>162</u>	SEWAGE: New ☐ Repair ☒
LOT <u>27</u>	86-146A
STREET _____	
NO. OF BEDROOMS <u>3</u>	WELL: New ☐ Deepen ☐
Owner: _____ Address: <u>7 E. Shore Rd.</u> Telephone: _____	
THIS APPLICATION WILL BE REVIEWED AND RETURNED WITHIN THE LEGAL TIME LIMIT OF 15 DAYS	

(NOTE: All Details of Construction Must Be Shown On A Separate Sheet)

Sewage: New ☐ Repair ☒

Contractor J. T. Excavating
Engineer 663-1479

1. Depth of Soil Log	<u>8'</u>	4. Date of Perc Test		7. No. of Saturations	
2. Depth of Ledge	<u>none</u>	5. Depth of Perc Test		8. Stabilized Rate-Min/Inch	
3. Depth of Water	<u>none</u>	6. No. of Holes		9. Distance Between Pits	

Type and Depths of Soil Encountered _____

Effect of Recent Rain or Lack of Rain on Perc Test _____

Apparent Moisture of Soil Prior to Perc Test _____

Liquid Disposal _____ Bed _____ Size _____ Pit ☒ Size 3'x6' No. 1

Septic Tank Capacities 1000 gallon No. 1

NOTE: Certification by Engineer of the Seasonally High Water Table Required On Separate Sheet. All Other Engineering Data Must Also Be Certified.

WELL: NEW ☐ DEEPENING ☐

CONTRACTOR _____

- No. of feet of casing _____
- Casing wall thickness _____
- Casing diameter _____
- Method of sealing _____

- Distance from nearest septic tank _____
- Dwellings served _____
- Driller's license & type _____



Sanitarian 10/14/86 C Deanna

J.T. EXCAVATING, INC.



663-1479

LOT 27

BLK. 162

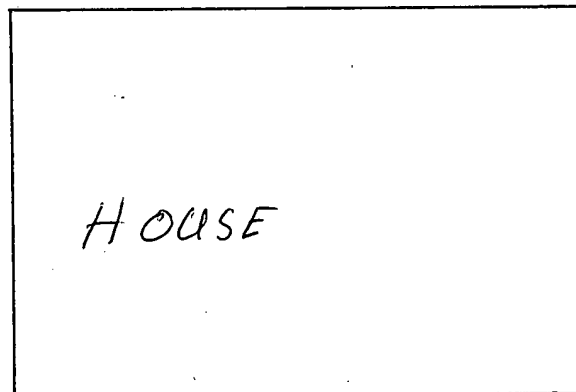

proposed
3'x6' seepage
pit



existing
6'x6' seepage pit

public water

7 E. Shore Rd.

PERMIT NO. _____

DATE OF ISSUE _____

BLOCK 162 LOT 27
STREET E. Shore Rd

INSPECTION RECORD — JEFFERSON TOWNSHIP DEPARTMENT OF HEALTH

SOIL LOG ☒

PERCOLATION _____

REPAIR WORK _____

for Addition of 1 Bedroom

Design Engineer _____

Builder _____

Contractor J.T. Ecker

Date Inspected 10/14/86

Comments:

~~18'~~ Hole dug 18'
6" x 6" x 2' 2"
7 1/2" Sandy Loam
No Water
No bedrock

To Final - 6' 6" x 3' pit connected to
existing system and

SEWAGE INSPECTIONS:

Excavation	Constructed	Final Grade	Other	Reinspection
	10/15/86 6' 6" x 3' pit <u>and</u>			

PERMIT NO. _____

DATE OF ISSUE _____

BLOCK <u>162</u>	LOT <u>27</u>
STREET <u>E. Shores Rd</u>	

INSPECTION RECORD — JEFFERSON TOWNSHIP DEPARTMENT OF HEALTH

SOIL LOG _____ PERCOLATION _____ REPAIR WORK X

Design Engineer _____ Builder Paul Burrows

Contractor J. Clark Date Inspected _____

Comments: _____

SEWAGE INSPECTIONS:

Excavation	Constructed	Final Grade	Other	Reinspection
	<u>9/2/75</u> 1000 gallon tank 6' x 6' pit at <u>(CP)</u>			

10/1/85

Memo

From
CINDEE LEVY

To Block 162, Lt 27

Advised owner that in order
to add bedroom, must upgrade
septic system by adding minimum
of 6' x 3' seepage pt.

