


Main Inspections Pipe Run

Project name:	Mainline ID:	City:	Address:
10/21/21 KEYPORT 3RD ST STORM	KEYPORT 3RD ST CB T11 TO ST T10	KEYPOT NJ	3RD ST
Start date/time:	Direction:	Weather:	Surface condition:
10/21/2021 10:33 AM	With the flow	Dry	Asphalt
Pipe shape:	Pipe material:	Pipe height:	Pipe width:
Circular	Clay	18.0 in.	

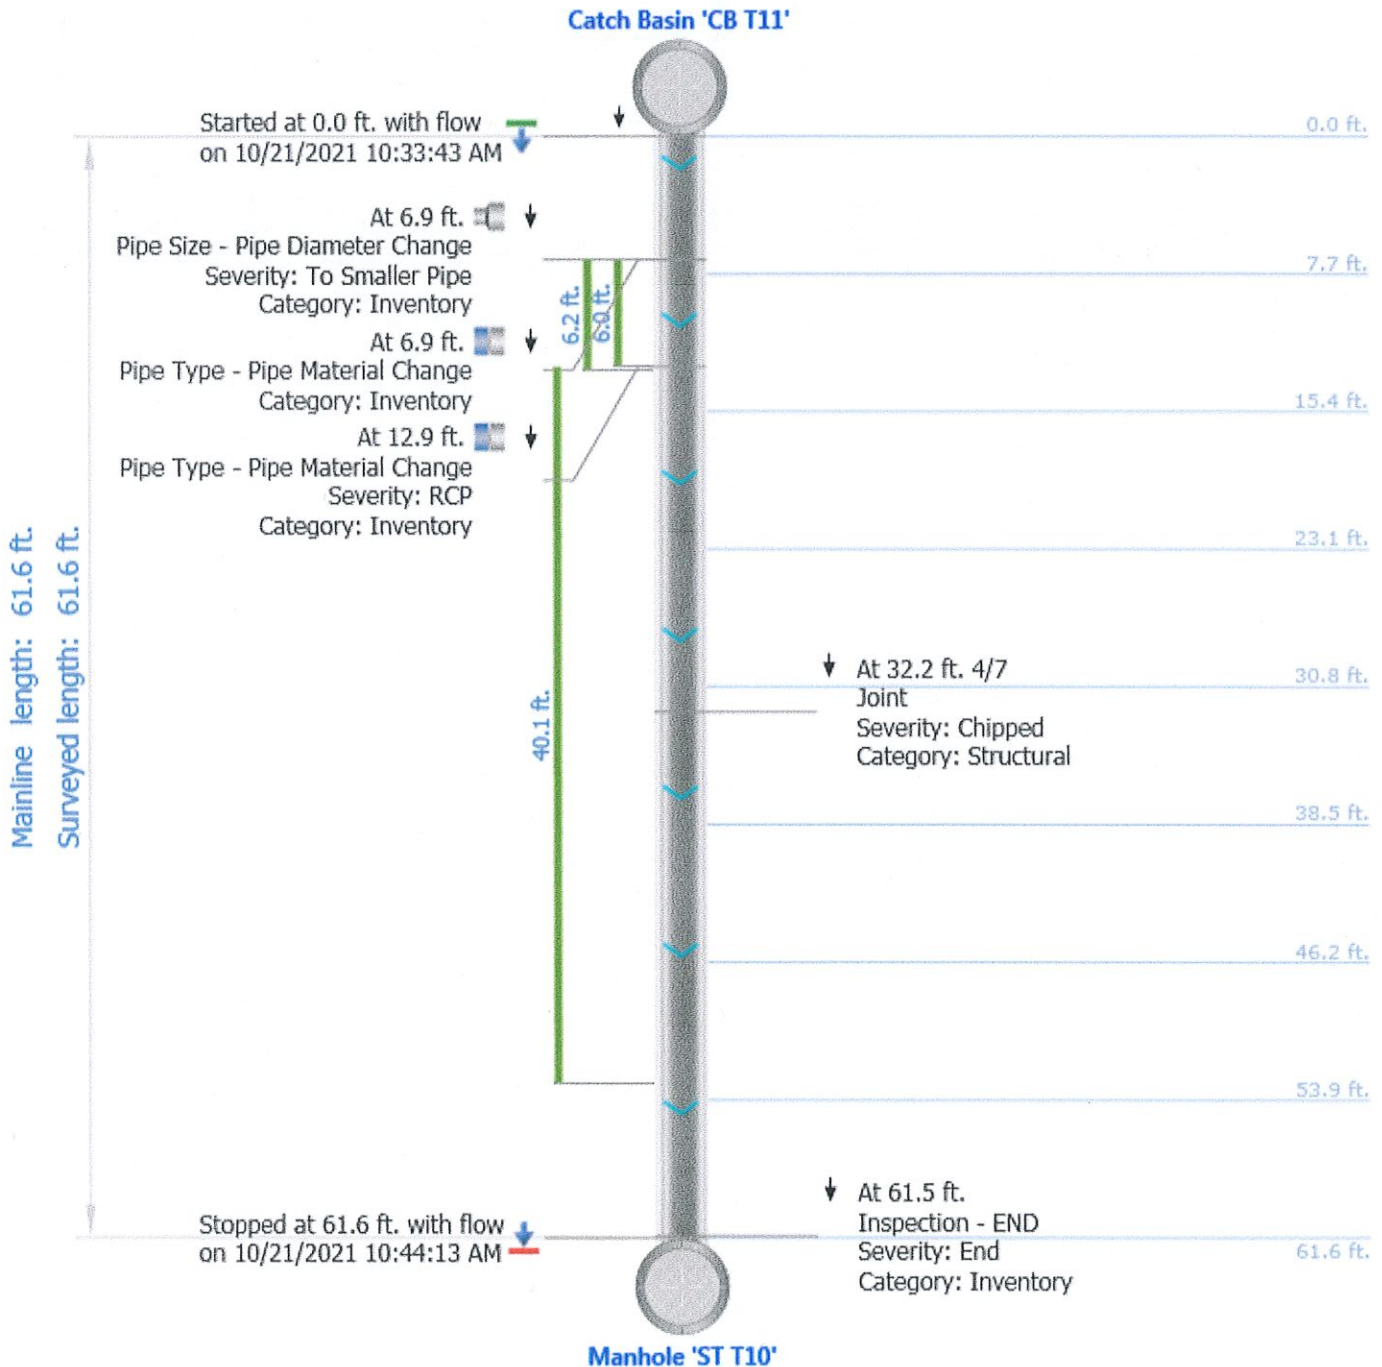

Main Inspections Small Photos

Mainline ID: KEYPORT 3RD ST CB T11 TO ST T10	City: KEYPOT NJ	Address: 3RD ST	Project name: 10/21/21 KEYPORT 3RD ST STORM
Start date/time: 10/21/2021 10:33 AM	Asset length: 61.6 ft.	Weather: Dry	Operator: John Read
Upstream node: CB T11	Depth US:	Downstream node: ST T10	Depth DS:
Pipe shape: Circular	Pipe material: Clay	Pipe height: 18.0 in.	Pipe width:
Comments:			


Observations

Distance	Dir.	Length	From/To	Code	Modifier/Severity	Rating	Comments
6.9 ft.	D	6.2 ft.	/	Pipe Type			
6.9 ft.	D	6.0 ft.	/	Pipe Size	To Smaller Pipe		
12.9 ft.	D	40.1 ft.	/	Pipe Type	RCP		
32.2 ft.	D		4 / 7	Joint	Chipped		
61.5 ft.	D		/	Inspection	End		

Inspection's photos

Main Inspections Pipe Run


Project name:	Mainline ID:	City:	Address:
10/21/21 KEYPORT 3RD ST STORM	KEYPORT 3RD ST ST T10 TO ST T6	KEYPOT NJ	3RD ST
Start date/time:	Direction:	Weather:	Surface condition:
10/21/2021 11:05 AM	With the flow	Dry	Asphalt
Pipe shape:	Pipe material:	Pipe height:	Pipe width:
Circular	Clay	15.0 in.	

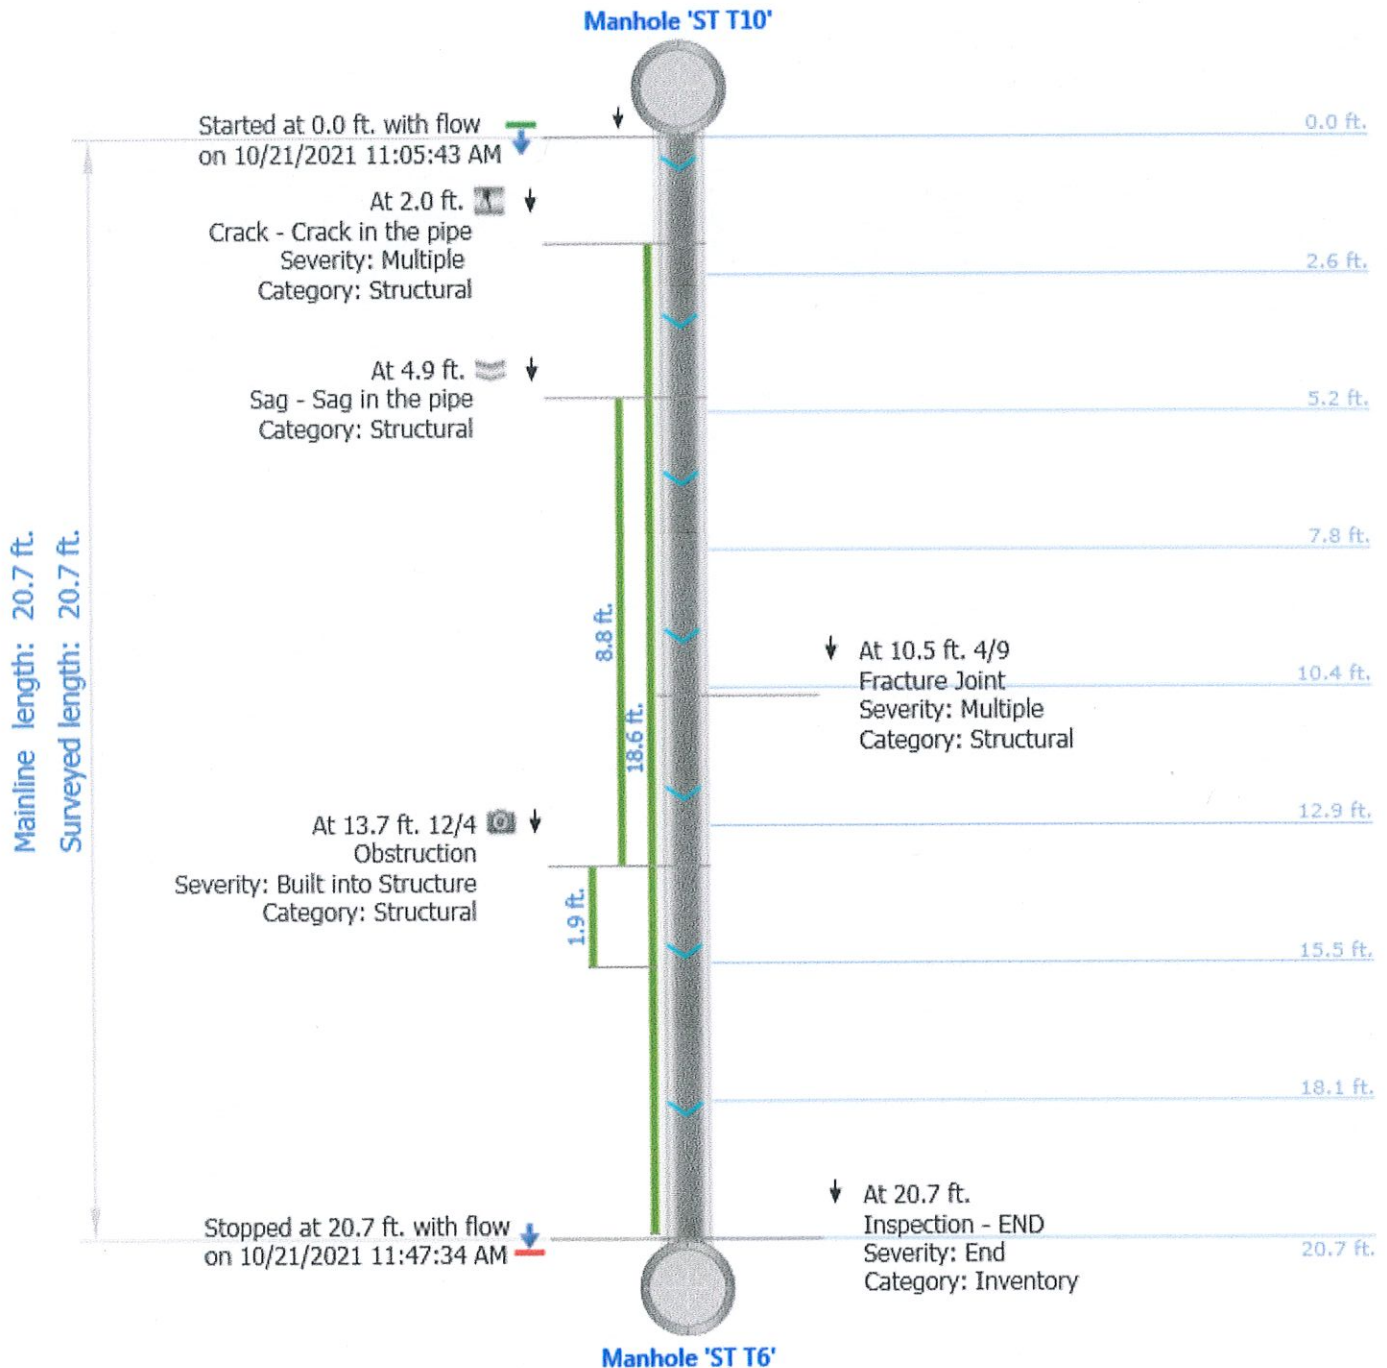

Main Inspections Small Photos

Mainline ID: KEYPORT 3RD ST ST T10 TO ST T6	City: KEYPOT NJ	Address: 3RD ST	Project name: 10/21/21 KEYPORT 3RD ST STORM
Start date/time: 10/21/2021 11:05 AM	Asset length: 20.7 ft.	Weather: Dry	Operator: John Read
Upstream node: ST T10	Depth US:	Downstream node: ST T6	Depth DS:
Pipe shape: Circular	Pipe material: Clay	Pipe height: 15.0 in.	Pipe width:
Comments:			


Observations

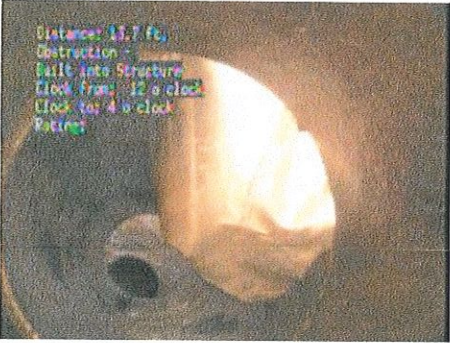Distance	Dir.	Length	From/To	Code	Modifier/Severity	Rating	Comments
2.0 ft.	D	18.6 ft.	/	Crack	Multiple		
4.9 ft.	D	8.8 ft.	/	Sag			
10.5 ft.	D		4 / 9	Fracture Joint	Multiple		
13.7 ft.	D	1.9 ft.	12 / 4	Obstruction	Built into Structure		
							
20.7 ft.	D		/	Inspection	End		

Inspection's photos

Main Inspections Pipe Run

Project name:	Mainline ID:	City:	Address:
10/21/21 KEYPORT 3RD ST STORM	KEYPORT 3RD ST T6 TO CB T7	KEYPOT NJ	3RD ST
Start date/time:	Direction:	Weather:	Surface condition:
10/21/2021 12:13 PM	With the flow	Dry	Asphalt
Pipe shape:	Pipe material:	Pipe height:	Pipe width:
Circular	Concrete Reinforced	30.0 in.	

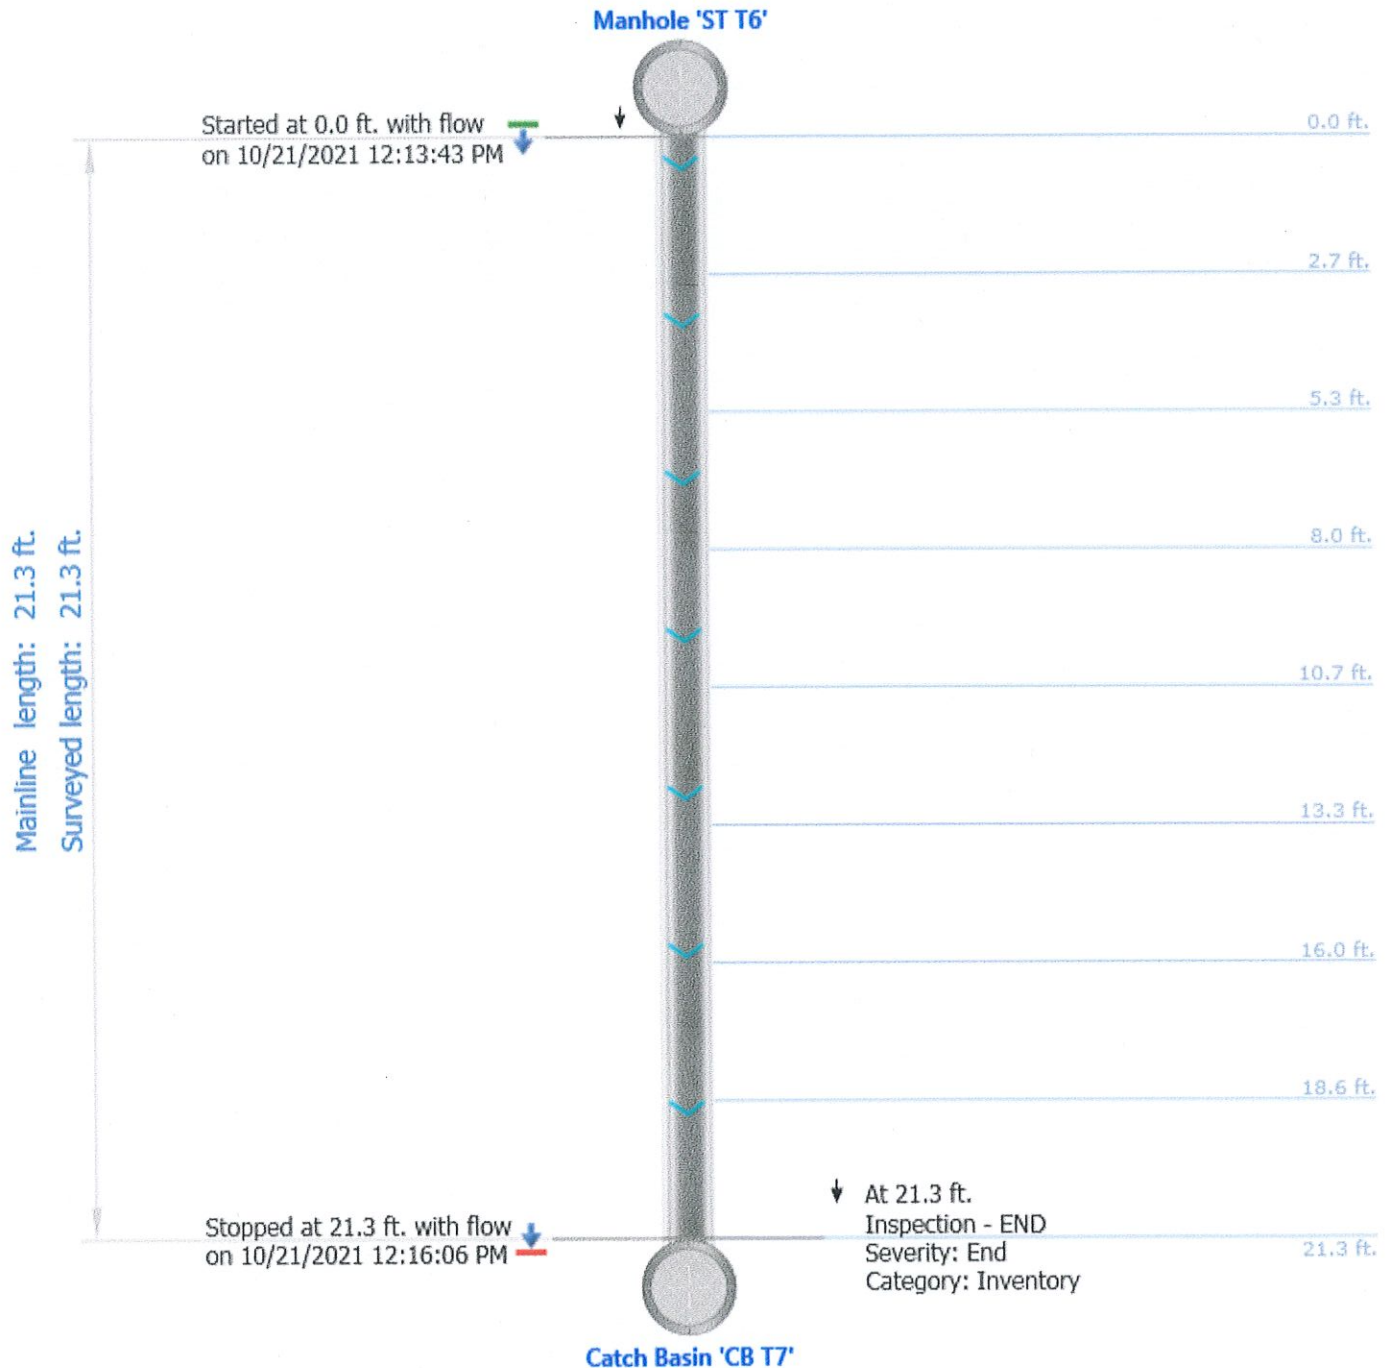

Main Inspections Small Photos

Mainline ID:	City:	Address:	Project name:
KEYPORT 3RD ST ST T6 TO CB T7	KEYPOT NJ	3RD ST	10/21/21 KEYPORT 3RD ST STORM
Start date/time:	Asset length:	Weather:	Operator:
10/21/2021 12:13 PM	21.3 ft.	Dry	John Read
Upstream node:	Depth US:	Downstream node:	Depth DS:
ST T6		CB T7	
Pipe shape:	Pipe material:	Pipe height:	Pipe width:
Circular	Concrete Reinforced	30.0 in.	
Comments:			


Observations

Distance	Dir.	Length	From/To	Code	Modifier/Severity	Rating	Comments
21.3 ft.	D		/	Inspection	End		

Inspection's photos

Main Inspections Pipe Run

Project name:	Mainline ID:	City:	Address:
10/21/21 KEYPORT 3RD ST STORM	KEYPORT 3RD ST CB T7 TO CB T4	KEYPOT NJ	3RD ST
Start date/time:	Direction:	Weather:	Surface condition:
10/21/2021 1:13 PM	With the flow	Dry	Asphalt
Pipe shape:	Pipe material:	Pipe height:	Pipe width:
Circular	Concrete Reinforced	30.0 in.	

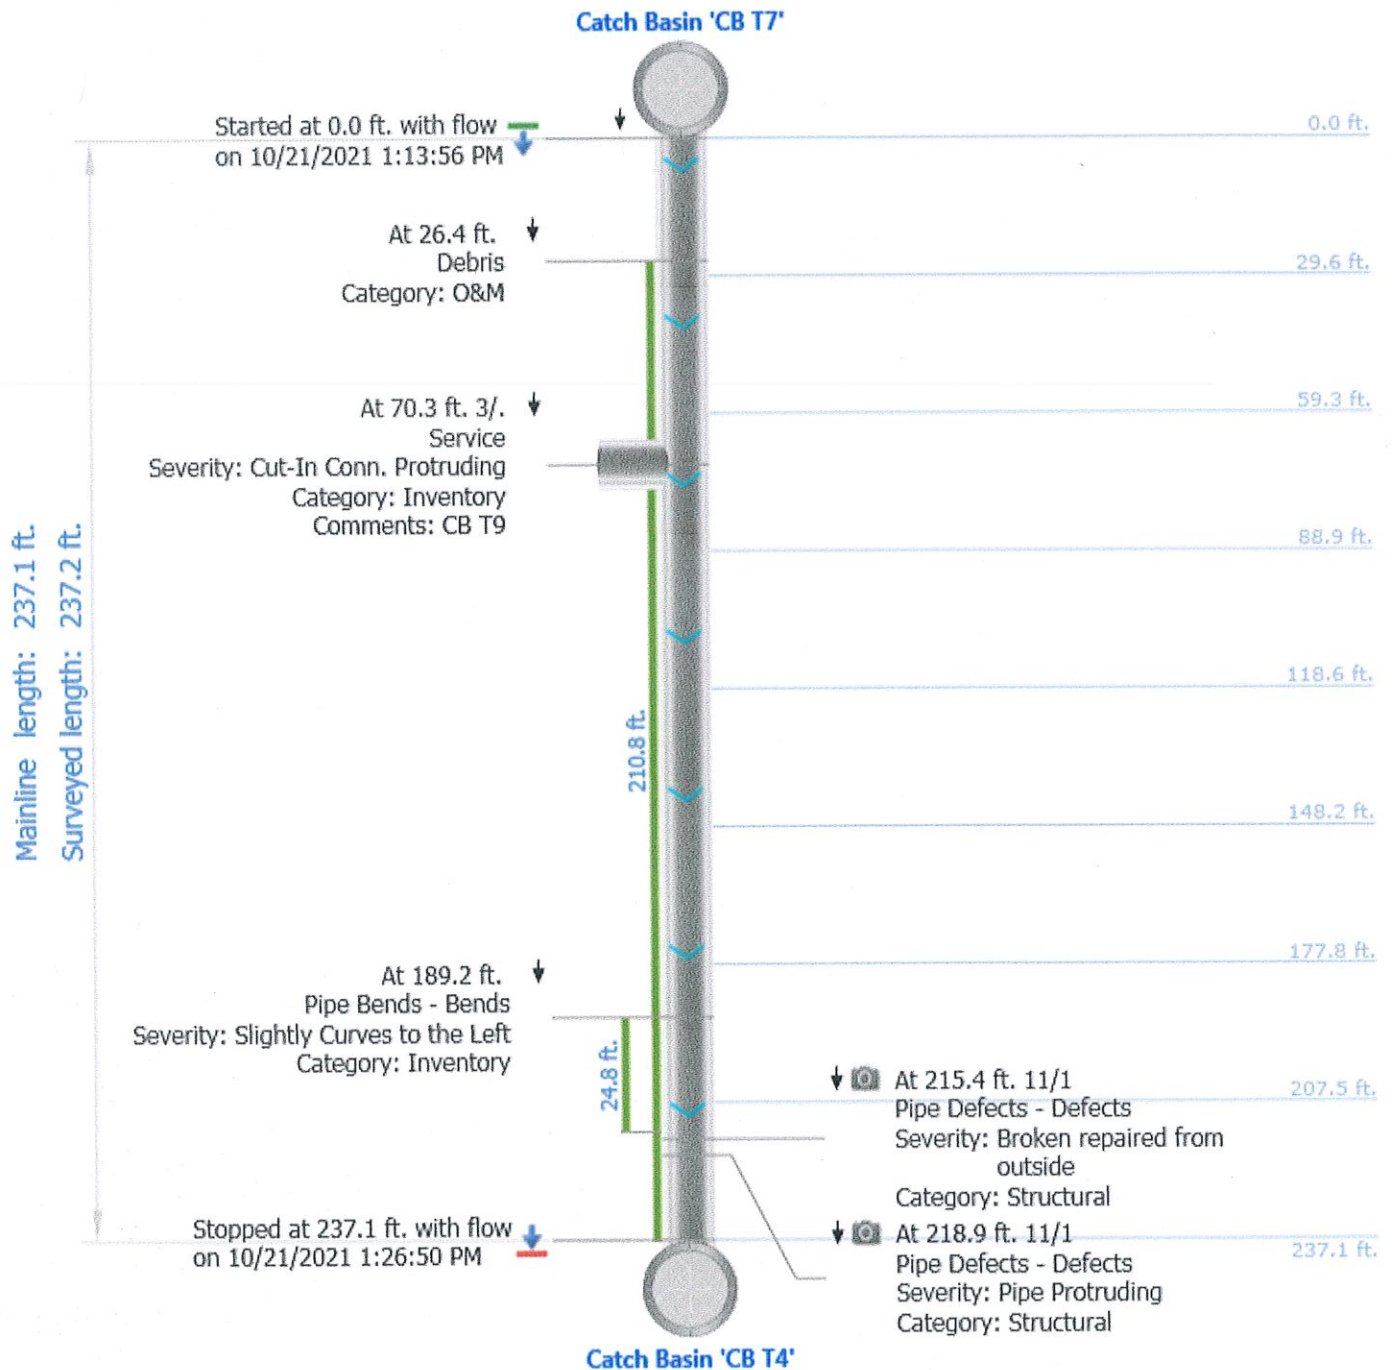

Main Inspections Small Photos

Mainline ID: KEYPORT 3RD ST CB T7 TO CB T4	City: KEYPOT NJ	Address: 3RD ST	Project name: 10/21/21 KEYPORT 3RD ST STORM
Start date/time: 10/21/2021 1:13 PM	Asset length: 237.1 ft.	Weather: Dry	Operator: John Read
Upstream node: CB T7	Depth US:	Downstream node: CB T4	Depth DS:
Pipe shape: Circular	Pipe material: Concrete Reinforced	Pipe height: 30.0 in.	Pipe width:
Comments:			



Observations


Distance	Dir.	Length	From/To	Code	Modifier/Severity	Rating	Comments
26.4 ft.	D	210.8 ft.	/	Debris			
70.3 ft.	D		3 /	Service	Cut-In Conn. Protruding		CB T9
189.2 ft.	D	24.8 ft.	/	Pipe Bends	Slightly Curves to the Left		
215.4 ft.	D		11 / 1	Pipe Defects	Broken repaired from outside		



Observations

Distance	Dir.	Length	From/To	Code	Modifier/Severity	Rating	Comments
218.9 ft.	D		11 / 1	Pipe Defects	Pipe Protruding		

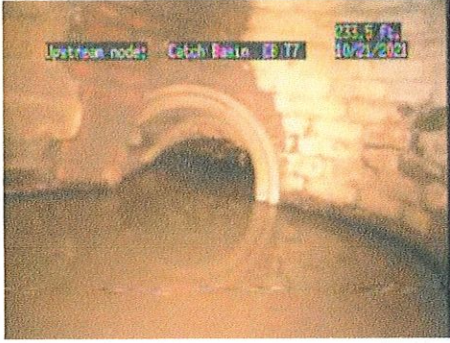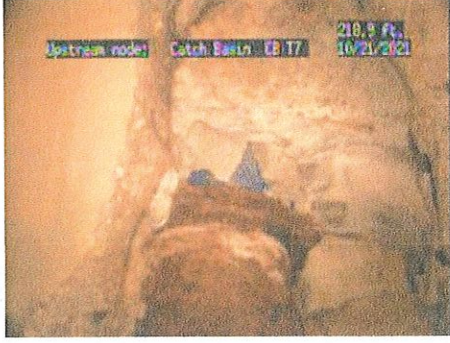


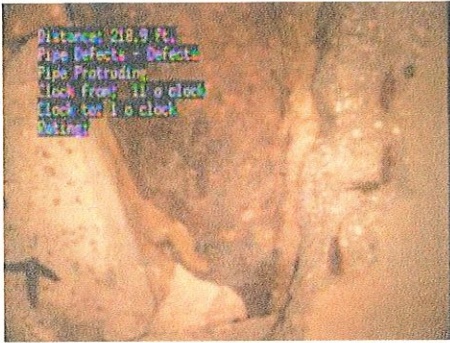



Inspection's photos

Main Inspections Pipe Run

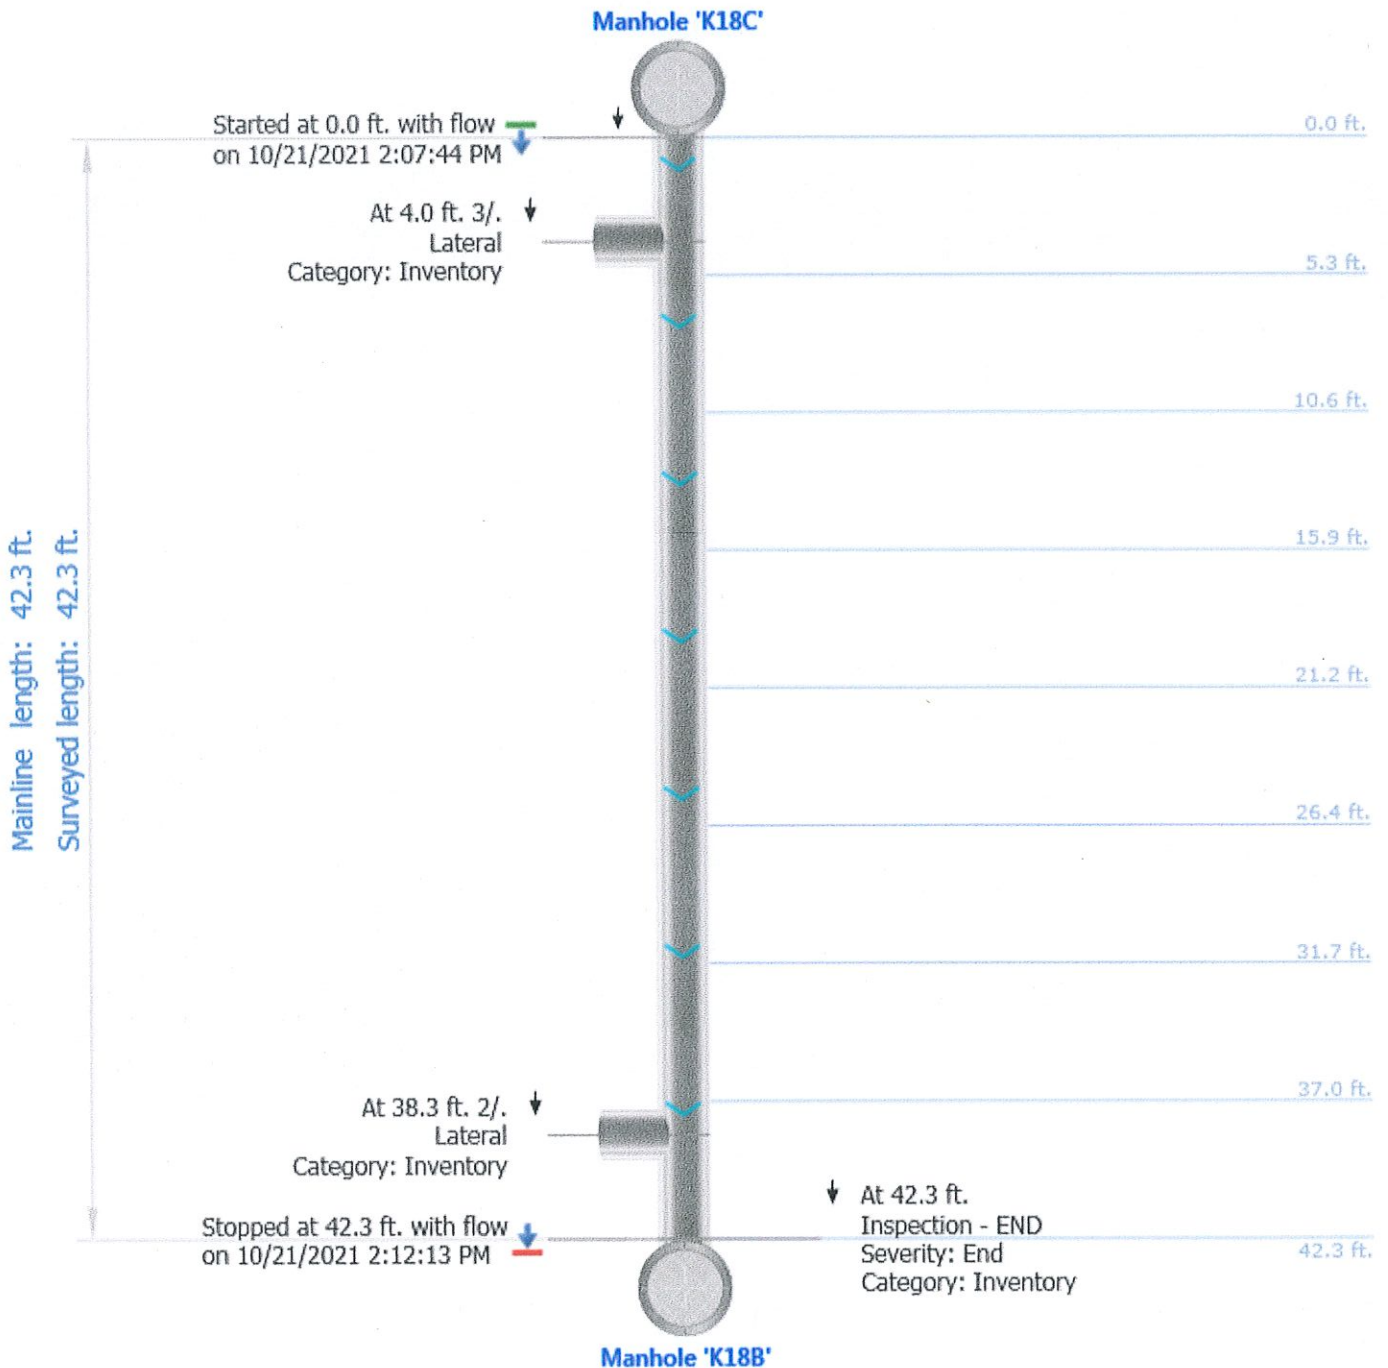Project name:	Mainline ID:	City:	Address:
10/21/21 KEYPORT 3RD ST STORM	KEYPORT HAVEN WAY K18C TO K18B	KEYPOT NJ	HAVEN WAY
Start date/time:	Direction:	Weather:	Surface condition:
10/21/2021 2:07 PM	With the flow	Dry	Asphalt
Pipe shape:	Pipe material:	Pipe height:	Pipe width:
Circular	PVC	8.0 in.	



Main Inspections Small Photos

Mainline ID: KEYPORT HAVEN WAY K18C TO K18B	City: KEYPOT NJ	Address: HAVEN WAY	Project name: 10/21/21 KEYPORT 3RD ST STORM
Start date/time: 10/21/2021 2:07 PM	Asset length: 42.3 ft.	Weather: Dry	Operator: John Read
Upstream node: K18C	Depth US: 	Downstream node: K18B	Depth DS:
Pipe shape: Circular	Pipe material: PVC	Pipe height: 8.0 in.	Pipe width:
Comments:			


Observations

Distance	Dir.	Length	From/To	Code	Modifier/Severity	Rating	Comments
4.0 ft.	D		3 /	Lateral			
38.3 ft.	D		2 /	Lateral			
42.3 ft.	D		/	Inspection	End		

Inspection's photos

Main Inspections Pipe Run

Project name:	Mainline ID:	City:	Address:
10/21/21 KEYPORT 3RD ST STORM	KEYPORT HAVEN WAY K18B TO K18A	KEYPOT NJ	HAVEN WAY
Start date/time:	Direction:	Weather:	Surface condition:
10/21/2021 2:12 PM	With the flow	Dry	Asphalt
Pipe shape:	Pipe material:	Pipe height:	Pipe width:
Circular	PVC	8.0 in.	

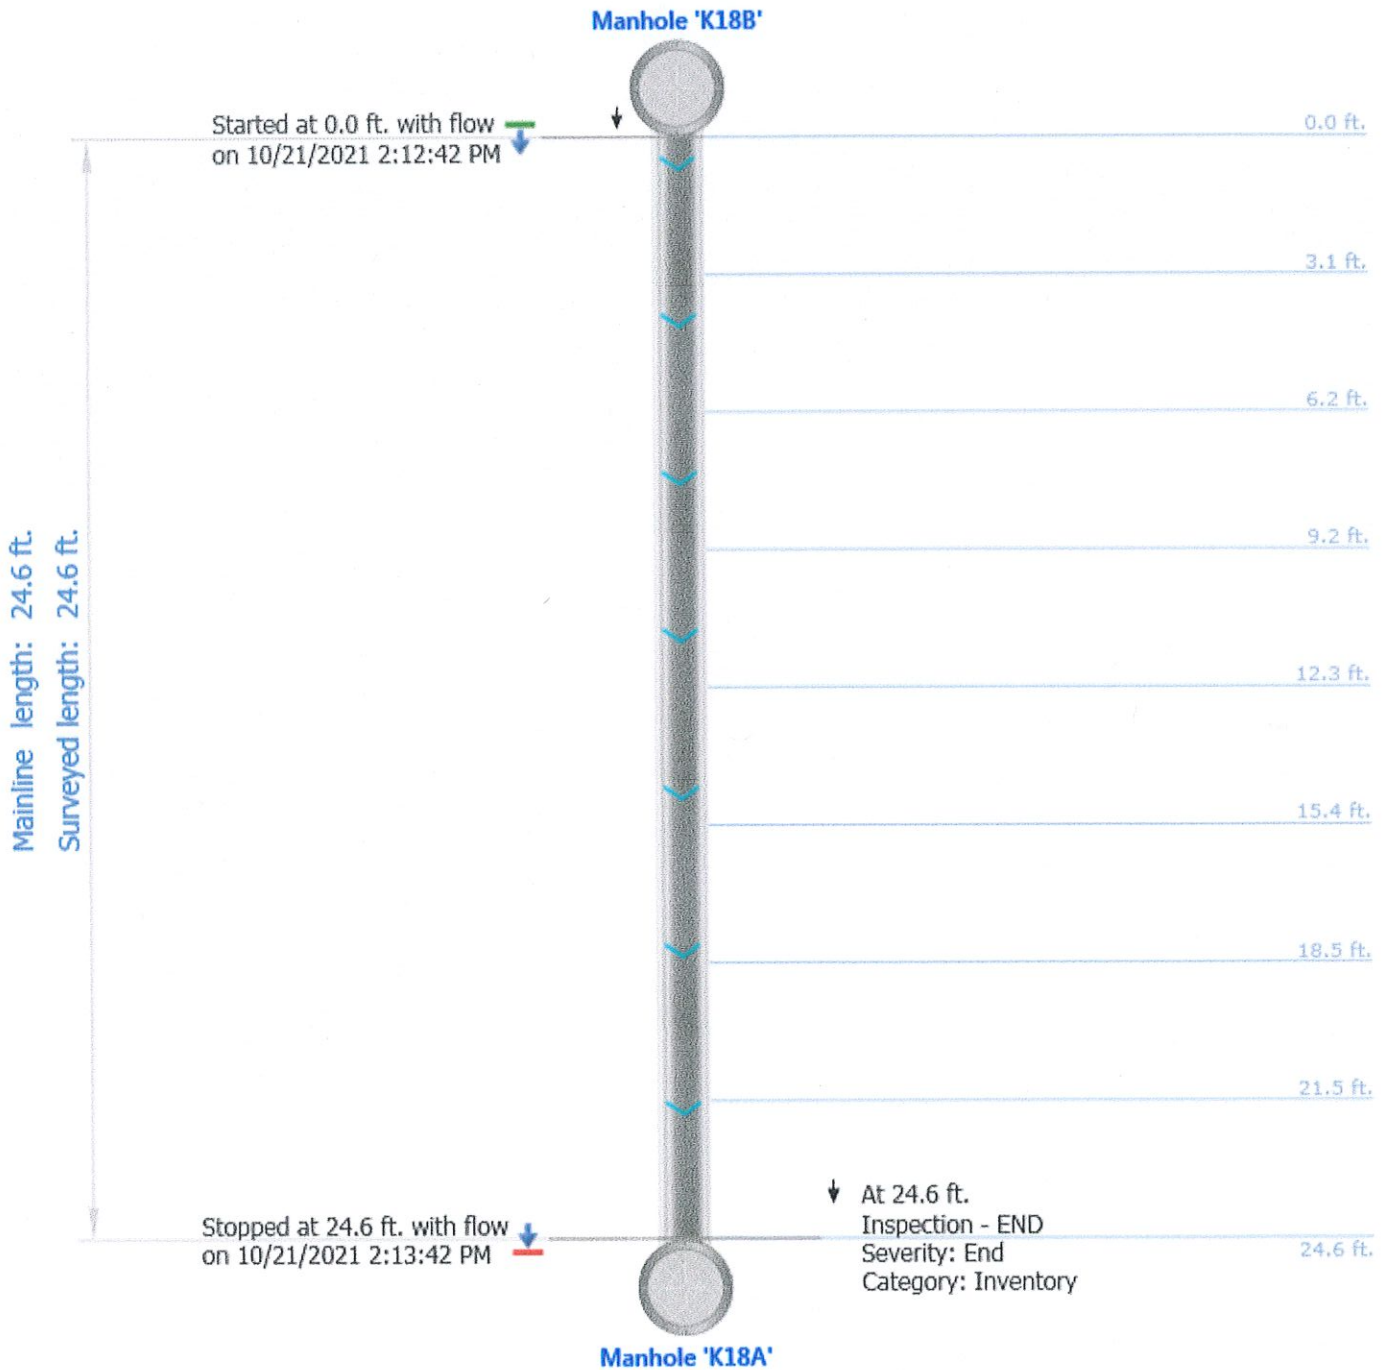

Main Inspections Small Photos

Mainline ID: KEYPORT HAVEN WAY K18B TO K18A	City: KEYPOT NJ	Address: HAVEN WAY	Project name: 10/21/21 KEYPORT 3RD ST STORM
Start date/time: 10/21/2021 2:12 PM	Asset length: 24.6 ft.	Weather: Dry	Operator: John Read
Upstream node: K18B	Depth US:	Downstream node: K18A	Depth DS:
Pipe shape: Circular	Pipe material: PVC	Pipe height: 8.0 in.	Pipe width:
Comments:			


Observations

Distance	Dir.	Length	From/To	Code	Modifier/Severity	Rating	Comments
24.6 ft.	D		/	Inspection	End		

Inspection's photos

Main Inspections Pipe Run

Project name: 10/21/21 KEYPORT 3RD ST STORM	Mainline ID: KEYPORT HAVEN WAY K18A TO K18	City: KEYPOT NJ	Address: HAVEN WAY
Start date/time: 10/21/2021 2:14 PM	Direction: With the flow	Weather: Dry	Surface condition: Asphalt
Pipe shape: Circular	Pipe material: PVC	Pipe height: 8.0 in.	Pipe width:

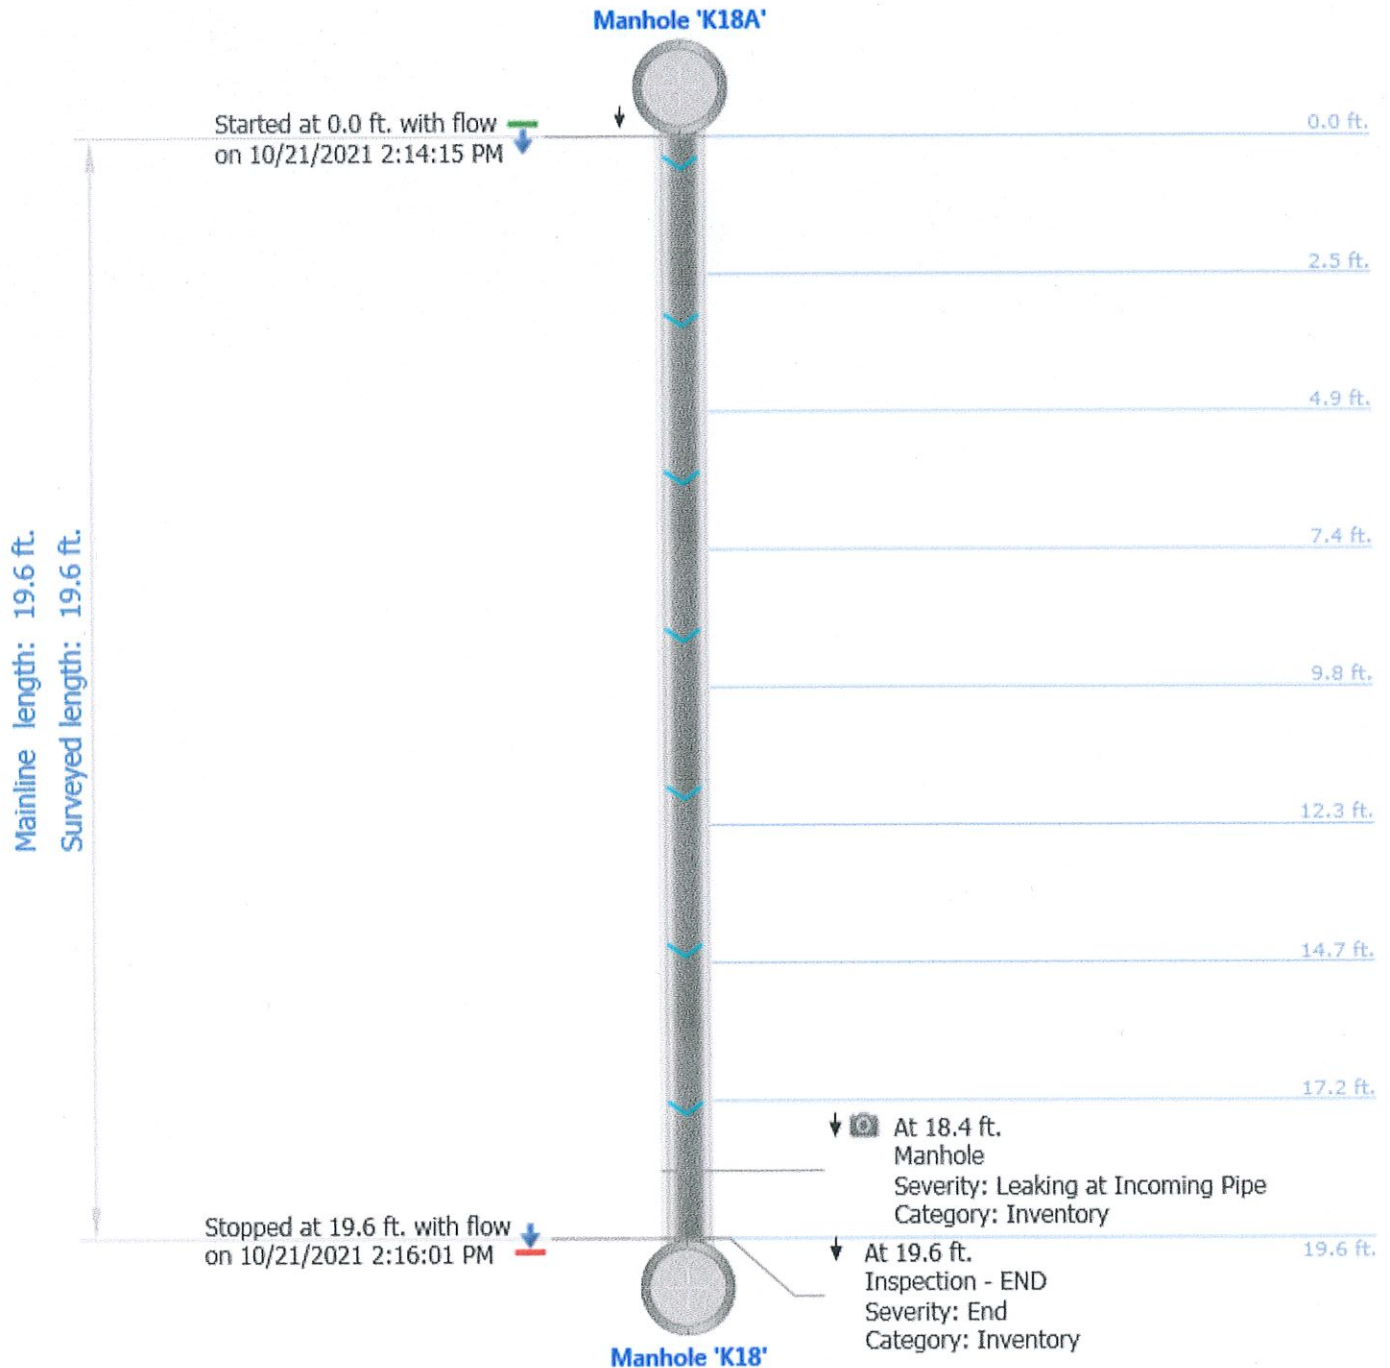


Main Inspections Small Photos

Mainline ID: KEYPORT HAVEN WAY K18A TO K18	City: KEYPOT NJ	Address: HAVEN WAY	Project name: 10/21/21 KEYPORT 3RD ST STORM
Start date/time: 10/21/2021 2:14 PM	Asset length: 19.6 ft.	Weather: Dry	Operator: John Read
Upstream node: K18A	Depth US: 	Downstream node: K18	Depth DS:
Pipe shape: Circular	Pipe material: PVC	Pipe height: 8.0 in.	Pipe width:
Comments:			

Observations

Distance	Dir.	Length	From/To	Code	Modifier/Severity	Rating	Comments
18.4 ft.	D		/	Manhole	Leaking at Incoming Pipe		

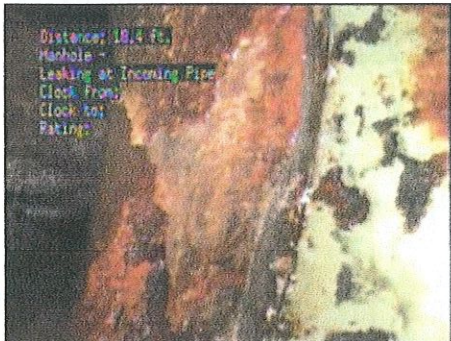


19.6 ft.	D		/	Inspection	End		
----------	---	--	---	------------	-----	--	--

Inspection's photos

Main Inspections Pipe Run

Project name: 10/21/21 KEYPORT 3RD ST KEYPORT HAVEN WAY STORM	Mainline ID: K18D TO K18C	City: KEYPOT NJ	Address: HAVEN WAY
Start date/time: 10/21/2021 2:18 PM	Direction: Against the flow	Weather: Dry	Surface condition: Asphalt
Pipe shape: Circular	Pipe material: PVC	Pipe height: 8.0 in.	Pipe width:

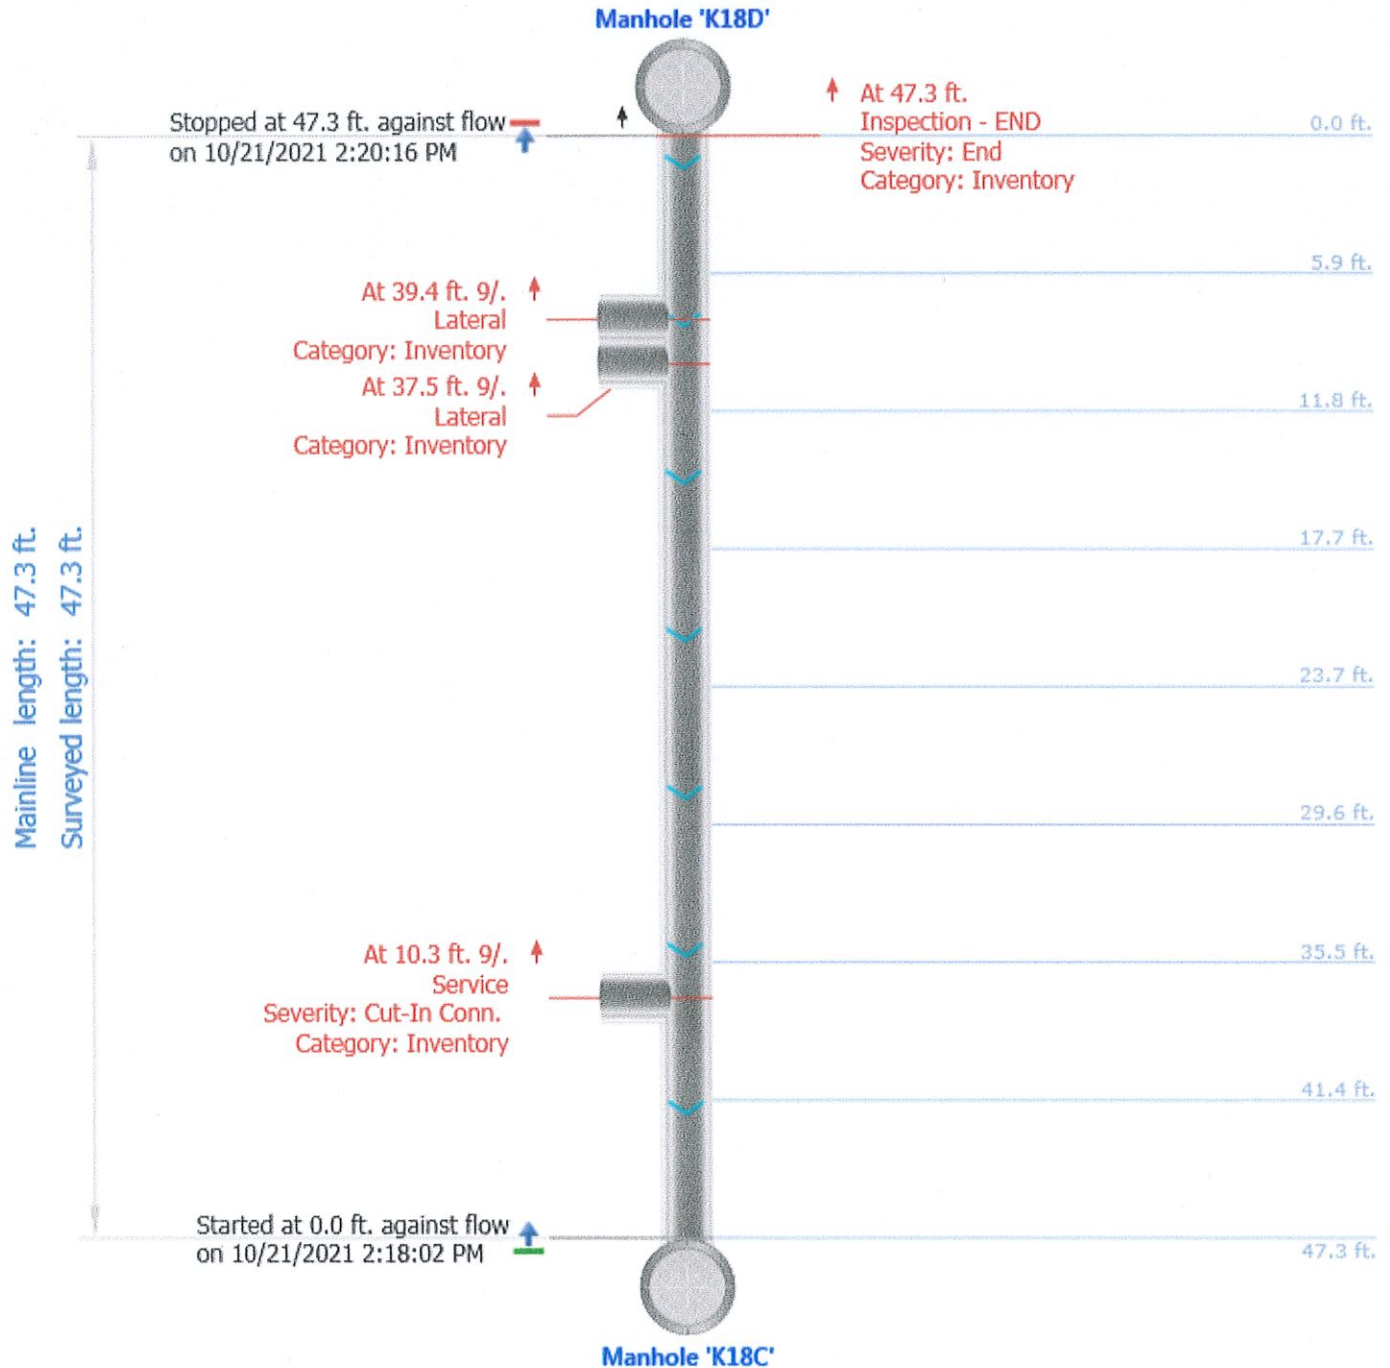

Main Inspections Small Photos

Mainline ID:	City:	Address:	Project name:
KEYPORT HAVEN WAY K18D TO K18C	KEYPOT NJ	HAVEN WAY	10/21/21 KEYPORT 3RD ST STORM
Start date/time:	Asset length:	Weather:	Operator:
10/21/2021 2:18 PM	47.3 ft.	Dry	John Read
Upstream node:	Depth US:	Downstream node:	Depth DS:
K18D		K18C	
Pipe shape:	Pipe material:	Pipe height:	Pipe width:
Circular	PVC	8.0 in.	
Comments:			

Observations

Distance	Dir.	Length	From/To	Code	Modifier/Severity	Rating	Comments
10.3 ft.	U		9 /	Service	Cut-In Conn.		
37.5 ft.	U		9 /	Lateral			
39.4 ft.	U		9 /	Lateral			
47.3 ft.	U		/	Inspection	End		

Inspection's photos

